AEE/SSD/SBE/000018/17-18
07-11-2017

Original/Duplicate/Triplicate

CONTRACT CERTIFICATE

(For Other Works)

Date.....2017

No. ***First & Final Bill***

Division: **BBMP, Dasarahalli**

Sub-Division: **BBMP, Shettyhalli**

Bill Received No. Dated

Schedule Docket No. Head of Account: **P1771**

Divisional / Sub Divisional

Cash Book Voucher No..... Dated.....

Work Code: 013-17-000026

Est.Cost: 15.00 Lakhs D.R.No. :

Name of Work (as per sanctioned estimate: **Establishing of R.O Plant near Mutthurayaswamy Temple Prashanth Nagara in Ward No. 13 in Shettyhalli Sub Division.**

Name of Contractor and Full Address: ***Sri. K. Shankar Reddy, Contractor, # 03, I[st] Cross, Eranna playa, Ramachandrapura Layout , Nagavara, Bangalore – 560 045.***

Reference to Agreement No. **EE/DD/BBMP/ WO/145/2015-17** Date: **24.03.2017**

Certified that the measurements were taken by me on 25/09/2017 and recorded of Pages 39801 to 39823 of measurement Book No. 59 and that the work is satisfactorily executed.

K. Sankar Reddy
Contractor

Officer-in-charge of work

Certified that the measurement were taken by me on 25/10/2017 and found correct. The work is satisfactorily executed.

Certified that the quantities of materials shown in column 3 of Account have been actually brought to site of the work and the contractor has not previously received any advance on this security. These materials are of and imperishable nature and are all required for immediate use on the work in connection with items for finished work have been agreed upon. A normal agreement signed and executed by the contractor is recorded in the office.

Sub-Division Officer

II Memorandum of Payment

1) Total value of work done or supplies made as per account within
2) Deduct amount to be held in reserve being .....percent Rs.....
3) " Balance
4) Deduct Payment:
   a. Amount of previous payment as in the Office Cash Book Voucher No.....Dated.....S.D. No.....Amount adjusted towards cash advance recovery of
   b. Payments Now made } cost store or other material supplied. recovery of amount creditable to this/other work. Amount paid on this bill Cheque / Cash.
5) Balance being unpaid value of work done held in reserve.
6) Deduct cash advance made on the Office cash Book Voucher No..... dated.....less adjustments.
7) Net amount due to or from Contractor unadjustments items.
8) Advance to Contractor for materials brought to site (as detailed) within.
9) Value of Government materials supplied.

1st and Final Bill Amount → 1400167=00
IT → 14002=00
LWC → 14002=00
LR → 16502=00
CBF → 1400=00
45906=00
Net → 1354261=00

Total amount adjusted -

K. Sankar Reddy
Contractor's Signature

Received Rs..... (in words).....
.....
by cash and by adjustment of Payment as per memorandum
(in final settlement of all demands)

(For use in the Office)

Witness
1.
2.

Dated Signature of Contractor K. Sankar Reddy

Paid by me by Cheque No.....Dated.....
Cash Rs.....
Dated.....

Initials of Officer making payment

Stamp

P.1771

Audited and admitted for Rs. 1400167=00
Passed by Cheque for Rs. 1354261=00
45906=00
by a/c.....
Executive Engineer
Accounts Officer
BBMP Dasarahalli Division

Scanned by CamScanner

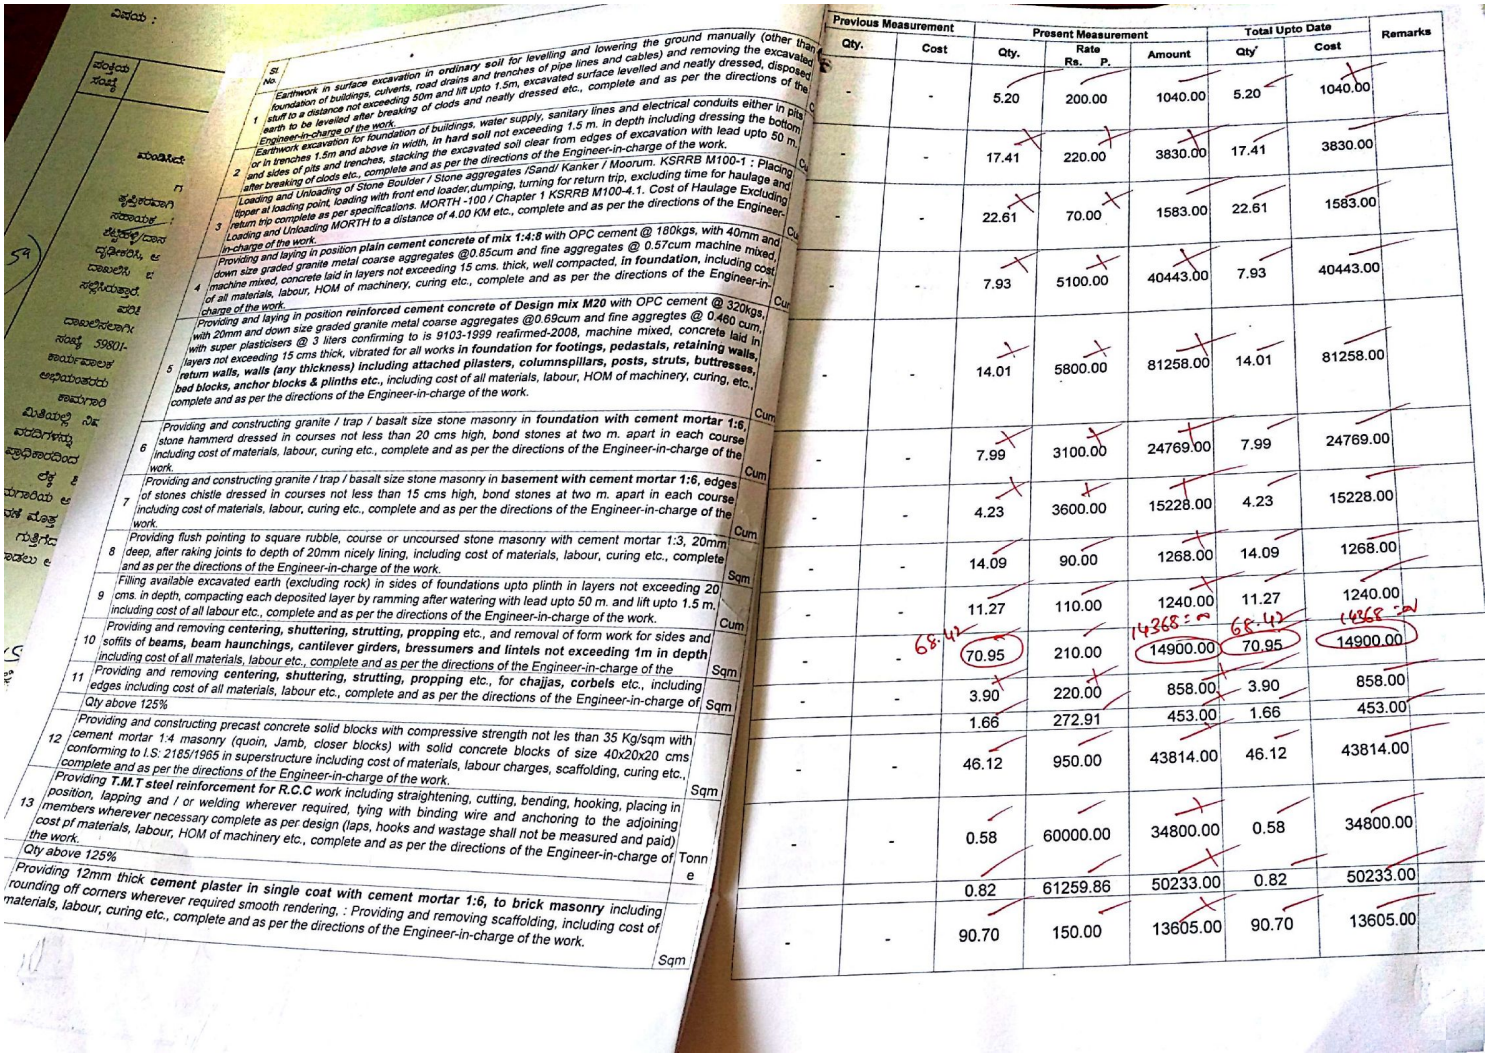

Sl No		Previous Measurement		Present Measurement			Total Upto Date		Remarks
		Qty.	Cost	Qty.	Rate Rs. P.	Amount	Qty	Cost	
1	Earthwork in surface excavation in **ordinary soil** for levelling and lowering the ground manually (other than foundation of buildings, culverts, road drains and trenches of pipe lines and cables) and removing the excavated stuff to a distance not exceeding 50m and lift upto 1.5m, excavated surface levelled and neatly dressed, disposed earth to be levelled after breaking of clods and neatly dressed etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	5.20	200.00	1040.00	5.20	1040.00	
2	Earthwork excavation for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, **in hard soil** not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. after breaking of clods etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	17.41	220.00	3830.00	17.41	3830.00	
3	Loading and Unloading of Stone Boulder / Stone aggregates /Sand/ Kanker / Moorum. KSRRB M100-1 : Placing tipper at loading point, loading with front end loader,dumping, turning for return trip, excluding time for haulage and return trip complete as per specifications. MORTH -100 / Chapter 1 KSRRB M100-4.1. Cost of Haulage Excluding Loading and Unloading MORTH to a distance of 4.00 KM etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	22.61	70.00	1583.00	22.61	1583.00	
4	Providing and laying in position **plain cement concrete of mix 1:4:8** with OPC cement @ 180kgs, with 40mm and down size graded granite metal coarse aggregates @0.85cum and fine aggregates @ 0.57cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, **in foundation**, including cost of all materials, labour, HOM of machinery, curing etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	7.93	5100.00	40443.00	7.93	40443.00	
5	Providing and laying in position **reinforced cement concrete of Design mix M20** with OPC cement @ 320kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregtes @ 0.460 cum, with super plasticisers @ 3 liters confirming to is 9103-1999 reafirmed-2008, machine mixed, concrete laid in layers not exceeding 15 cms thick, vibrated for all works **in foundation for footings, pedastals, retaining walls, return walls, walls (any thickness) including attached pilasters, columnspillars, posts, struts, buttresses, bed blocks, anchor blocks & plinths etc.,** including cost of all materials, labour, HOM of machinery, curing, etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	14.01	5800.00	81258.00	14.01	81258.00	
6	Providing and constructing granite / trap / basalt size stone masonry in **foundation with cement mortar 1:6,** stone hammerd dressed in courses not less than 20 cms high, bond stones at two m. apart in each course including cost of materials, labour, curing etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	7.99	3100.00	24769.00	7.99	24769.00	
7	Providing and constructing granite / trap / basalt size stone masonry in **basement with cement mortar 1:6,** edges of stones chistle dressed in courses not less than 15 cms high, bond stones at two m. apart in each course including cost of materials, labour, curing etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	4.23	3600.00	15228.00	4.23	15228.00	
8	Providing flush pointing to square rubble, course or uncoursed stone masonry with cement mortar 1:3, 20mm deep, after raking joints to depth of 20mm nicely lining, including cost of materials, labour, curing etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	14.09	90.00	1268.00	14.09	1268.00	
9	Filling available excavated earth (excluding rock) in sides of foundations upto plinth in layers not exceeding 20 cms. in depth, compacting each deposited layer by ramming after watering with lead upto 50 m. and lift upto 1.5 m. including cost of all labour etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	11.27	110.00	1240.00	11.27	1240.00	
10	Providing and removing **centering, shuttering, strutting, propping** etc., and removal of form work for sides and soffits of **beams, beam haunchings, cantilever girders, bressumers and lintels not exceeding 1m in depth** including cost of all materials, labour etc., complete and as per the directions of the Engineer-in-charge of the	-	-	70.95	210.00	14900.00	70.95	14900.00	
11	Providing and removing **centering, shuttering, strutting, propping** etc., for **chajjas, corbels** etc., including edges including cost of all materials, labour etc., complete and as per the directions of the Engineer-in-charge of	-	-	3.90	220.00	858.00	3.90	858.00	
	Qty above 125%			1.66	272.91	453.00	1.66	453.00	
12	Providing and constructing precast concrete solid blocks with compressive strength not les than 35 Kg/sqm with cement mortar 1:4 masonry (quoin, Jamb, closer blocks) with solid concrete blocks of size 40x20x20 cms conforming to I.S: 2185/1965 in superstructure including cost of materials, labour charges, scaffolding, curing etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	46.12	950.00	43814.00	46.12	43814.00	
13	Providing **T.M.T steel reinforcement for R.C.C** work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid) cost pf materials, labour, HOM of machinery etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	0.58	60000.00	34800.00	0.58	34800.00	
	Qty above 125%			0.82	61259.86	50233.00	0.82	50233.00	
	Providing 12mm thick **cement plaster in single coat with cement mortar 1:6, to brick masonry** including rounding off corners wherever required smooth rendering, : Providing and removing scaffolding, including cost of materials, labour, curing etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	90.70	150.00	13605.00	90.70	13605.00	

Scanned by CamScanner

		Qty above 125%									
15		Hinges 5" Heavy Duty									
16		Bottom Lock Nail									
17		MS Clamps									
18		Brass Screws 25 mm									
19		Providing and fixing **Single shutter glass door** of 12mm thick plain toughened glass (Saint Gobain, Modi float). The door is fixed by using any approved make hardware fitting like patch fitting, pivot, floor machine, locking arrangements and suitable SS door rails with floral glass etching for 1/3 portion of door area etc complete. The rate includes cost of all materials, labour, hire of tools & machineries,and etc., complete and as per the directions of the Engineer-in-charge of the work.									
20		Providing precast chequered mosaic tiles dark shade using ordinary grey cement for steps and flooring, with precast 20mm thick, using marble chips of 7 to 10 nominal size laid in floors, steps and landings on a bed of 12mm thick cement mortar 1:3 mix, and jointed with neat cement slurry mixed with pigment to match the shade of tiles, curing, rubbing, polishing, oxalic acid wash, wax polish , including cost of materials, labour, etc., complete and as per the directions of the Engineer-in-charge of the work.									
21		Providing and laying flooring using **prepolished, water cut/gang saw 19mm thick granite** laid over bed of 20mm thick 1:4 cm & jointed with neat cement slurry mixed with pigment to mach shade of granite slabs including laying POP on finished surface and cleaning the surface, including the cost of all materials and labours etc., complete as per specifications. - **using silver grey granite / Multy Red / Ruby Red / Black / HassanGreen Granite of width not less than 900mm** etc., complete and as per the directions of the Engineer-in-charge of the work.									
22		Providing flooring with 60 cms.x 60 cms. size Vitrified glazed tiles of approved quality & make, fixed on top of existing flooring fixed with suitable adhesive, including cutting the tiles to the required size and fixing etc., complete and as per the directions of the Engineer-in-charge of the work.									
23		Applying priming coat over new wood surface and / or wood based surface after brushing with wood primer pink paint including preparing the surface after thoroughly cleaning oil, grease, dirt and foreign matter, sand papering and knotting ready mix paint including cost of materials, labour, etc., complete and as per the directions of the Engineer-in-charge of the work.									
24		Providing and applying painting two coats (excluding priming coat) on new wood surface and / or wood based surface with enamel paint to give an even shade, cleaning the surface of all dirt, dust and foreign matter, sand papering including cost of materials, labour, etc., complete and as per the directions of the Engineer-in-charge of the work.									
25		Providing and applying painting in two coats with plastic emulsion paint of approved brand on wall surface to give an even approved shade after thoroughly brushing the surface, free from mortar drops and other foreign matter including preparing the surface even and sand paper smooth, cost of materials, labour, complete as per specifications. - with primer etc., complete and as per the directions of the Engineer-in-charge of the work.									
		Qty above 125%									
26		Providing and finishing external walls in two coats with waterproof cement paint of approved brand and shade to give an even shade after throughly brooming the surface to remove all dirt and loose powdered material, free from mortar drops and other foreign matter cost of materials, labour, etc., complete and as per the directions of the Engineer-in-charge of the work.									
		Qty above 125%									
27		POP Sheets Corogated Roof Sheets nut Bolts including labour charges etc complete									
28		GI Roof Sheets fixing and complete including labour charges									
29		Steel pre fabricates structure with a 14 Guage (3") each 60 kg including cutting and transportation complete									
30		Supplying and wiring adopting loop system in existing PVC Conduit / casing capping using 1100V grade, COPPER conductor flexible multistrand FRLS PVC insulated, 2 X1.5Sq.mm Cable confirming to the GTP, with a 6Amps flush type SP control switch shall be fixed on the existing plastic sheet / gang box, the other end of the wires shall be terminated with sufficient loose length in a wood/PVC round block. complete for each outlet. GROUP A b) Short point upto 3Mtr from tapping point to out let via switch etc., complete and as per the directions of the Engineer-in-charge of the work.									
31		b) Medium point above 3Mtr upto 6Mtr from tapping point to out let via switch									
32		c) Long point above 6Mtr upto 10Mtr from tapping point to out let via switch									

Previous Measurement			Present Measurement			Total Upto Date		
Qty.	Cost	Qty.	Rate Rs. P	Amount	Qty	Cost	Remarks
-	-	34.26	151.62	5195.00	34.26	5195.00	
-	-	4.00	37.00	148.00	4.00	148.00	
-	-	10.00	47.00	470.00	10.00	470.00	
-	-	8.00	38.00	304.00	8.00	304.00	
-	-	50.00	2.10	105.00	50.00	105.00	
-	-	8.80	9400.00	82720.00	8.80	82720.00	
-	-	5.49	880.00	4831.00	5.49	4831.00	
-	-	0.00	0.00	0.00	0.00	0.00	
-	-	14.75	880.00	12980.00	14.75	12980.00	
-	-	6.48	30.00	194.00	6.48	194.00	
-	-	6.48	80.00	518.00	6.48	518.00	
-	-	41.80	90.00	3762.00	41.80	3762.00	
		23.80	90.97	2165.00	23.80	2165.00	
-	-	12.50	90.72	1134.00	12.50	1134.00	
		53.34	84.90	4529.00	53.34	4529.00	
-	-	0.00	0.00	0.00	0.00	0.00	
-	-	0.00	0.00	0.00	0.00	0.00	
-	-	0.00	0.00	0.00	0.00	0.00	
-	-	2.00	114.00	228.00	2.00	228.00	
-	-	2.00	215.00	430.00	2.00	430.00	
-	-	2.00	334.00	668.00	2.00	668.00	

Scanned by CamScanner

Sl. No.			Previous Measurement		Present Measurement			Total Upto Date		
			Qty.	Cost	Qty.	Rate Rs. P.	Amount	Qty	Cost	Remarks
33	Supplying heavy gauge PVC conduit pipe .....dia .....mm thick confirming to IS 2509 with suitable size bends, junction boxes, adhesive paste etc., and fixing using inverted wood plugs in case of RCC ceiling and RCC wall / stone structure or rawl plugs in case of brick walls and cement plastering the damaged portion using heavy gauge saddles at an interval of 700mm using NF screws. 19/20mm dia 2mm thick etc., complete and as per the directions of the Engineer-in-charge of the work.	M	-	-	15.00	54.00	810.00	15.00	810.00	
34	Wiring for lighting/power circuit using one of FRLS PVC insulated 1100V grade, multistrand Copper with low conductor resistance single core wire in open or concealed system of wiring with specified IS-694:1990 & confirming to GTP of GROUP -A. 2.5.2) 1.5 Sqmm etc., complete and as per the directions of the Engineer-in-charge of the work.	M	-	-	5.00	18.60	93.00	5.00	93.00	
35	2.5.1) 1 Sqmm	M	-	-	5.00	13.00	65.00	5.00	65.00	
36	2.5.3) 2.5 Sqmm	M	-	-	5.00	29.20	146.00	5.00	146.00	
37	2.5.4) 4 Sqmm	M	-	-	2.00	42.10	84.00	2.00	84.00	
38	Supplying and flush mounting teak wooden box without front plank, made of not less than 12mm thick wood, after due groove cutting, Finishing with necessary cement plastering complete (1.6.3) 10"x7"x3" (254x178x76mm) etc., complete and as per the directions of the Engineer-in-charge of the work.	M	-	-	2.00	87.00	174.00	2.00	174.00	
39	(1.6.4) 8"x6"x3" (203x152x76mm)	Ea	-	-	1.00	73.00	73.00	1.00	73.00	
40	(1.6.1)12"x12"x3" (300x300x76mm)	Ea	-	-	1.00	116.00	116.00	1.00	116.00	
41	Supplying 4mm thick plastic sheet with necessary nitches for fixing switches, regulators etc., and fixing on existing wooden or metal box using N.F. screws etc., complete and as per the directions of the Engineer-in-charge of the work.	Ea	-	-	1225.00	0.25	306.00	1225.00	306.00	
42	Supplying and fixing/replacing of 6/16/32Amps electrical accessories on existing switch board. GROUP A 3.15.1) 6 Amps SP Switch etc., complete and as per the directions of the Engineer-in-charge of the work.	Sc	-	-	1.00	35.00	35.00	1.00	35.00	
43	3.15.3) 6 Amps 3 Way 5 Pin Socket	No	-	-	1.00	53.00	53.00	1.00	53.00	
44	3.15.6) 6 Amps Lamp Holder	No	-	-	3.00	48.00	144.00	3.00	144.00	
45	3.15.13) 16/6 Amps combined plug and socket with control switch	No	-	-	3.00	268.00	804.00	3.00	804.00	
46	Supplying and fixing of modular switch/ Socket/stepped electronic fan regulator/ dimmer/telephone socket etc on existing modular switch plate as per IS 3854 and IS 1293 GROUP B 3.7.18) 1000-1200 Watts Dimmer etc., complete and as per the directions of the Engineer-in-charge of the work.	No	-	-	1.00	447.00	447.00	1.00	447.00	
47	Supplying and fixing miniature circuit breakers on existing MCB distribution boards using necessary fixing materials and 'C' Type curve, indicator ON/OFF, energy cross-3 with Short circuit breaking capacity of 10K and complete wiring as required confirming to IEC 60898. 6.16.1) 5-32 Amps SP etc., complete and as per the directions of the Engineer-in-charge of the work.	Eac	-	-	1.00	415.00	415.00	1.00	415.00	
48	Supplying, fixing, wiring, earth electrode for grounding conduits, I.C. cutouts and other equipment's on the meter board using 40mm dia 2.90mm thick GI pipe 2.5 mtr long buried in a pit ... The pit should be filled with equal proportion of salt and charcoal 150mm all-round the pipe to complete depth. The connection from the pipe to the conduit etc., is to be established through GI wire of size as per ISI specification 7.3.3. of IS 732 using 12mm dia bolts, nuts, washers and check nuts etc., the pipe shall have 16 through holes of 122 mm dia etc., complete and as per the directions of the Engineer-in-charge of the work.	Eac	-	-	1.00	2500.00	2500.00	1.00	2500.00	
49	6.7 Supplying & fixing of Porcelain fuse channel with cut out on existing wooden/panel using necessary nuts, bolts and washers etc., complete and as per the directions of the Engineer-in-charge of the work.	No	-	-	1.00	120.00	120.00	1.00	120.00	
0	Supplying patti type fluorescent tube light fitting of 2' - suitable for 14 watts fluorescent tube fitting, made out of M.S. Sheet and stove enameled with HF Electronic Ballast , locking type brass contact holders mounted on double fold type sheet base fully wired for use on 230 volts AC . Supply including T5 lamp etc., complete and as per the directions of the Engineer-in-charge of the work.	Eac	-	-	5.00	450.00	2250.00	5.00	2250.00	
	Fixing all types and all capacities of fluorescent / false ceiling / spot light / CFL / LED fittings indoor on the wall / ceiling / rafters / girders using 23/0.0076" twin twisted PVC insulated wires, required Nos of round blocks and clamps. 17.7.1) On wall / ceiling / Rafter / Girders etc., complete and as per the directions of the Engineer-in-charge of the work.	Eac	-	-	5.00	90.00	450.00	5.00	450.00	
	Short Poles : (Shereas clearance between Messenger wire and ground is inadequate) a) Supplying and fixing 40mm dia 2.90 thick GI pipe 1.8m long complete with atleast 2 GI pipe 1.8 m long complete with ateast 2 nos of through bolts 12mm dia with MS back plate 100 x 100 x 6 mm dia with eye bolt fixed at top deadeninding messenger wire with masonary patch work etc complete as per approved drawing (for single phase installations etc., complete and as per the directions of the Engineer-in-charge of the work.	Eac	-	-	1.00	480.00	480.00	1.00	480.00	

Scanned by CamScanner

Sl. No.		Previous Measurement		Present Measurement			Total Upto Date		
		Qty.	Cost	Qty.	Rate Rs. P.	Amount	Qty	Cost	Remarks
53	INSULATED CABLE ON MESSENGER WIRE Using 2 single core wires for a single phase and 4 single core wires for 3 phase. Supplying and stringing PVC insulated and PVC sheathed 650/1100V class aluminium conductor of size supported by 3.15mm (10 SWG) GI messenger wire with two break insulators one at each end of the span with suspenders at intervals of 0.75m. Each suspender shall be of porcelain reel insulator of suitable core through which insulated wire passes(single core or twin core as the case may be) and this reel insulator shall be fixed to the messenger wire using 2mm (No.14SWG) GI wire suitably bent and twisted. Separate reely insulator shall be provided for each wire, the messenger wire shall be ded-ended on the clamp provided to the departmental pole wide etc., complete and as per the directions of the Engineer-in-charge of the work.	-	-	30.00	60.00	1800.00	30.00	1800.00	
	10000 LPD R.O. Plant								
54									
	RAW WATER PUMP:								
	Quantity : 1No.								
	Type: Centrifugal Mono Block								
	MOC & Make : UKL								
	Motor Rating : 0.75 HP								
	PRESSURE SAND FILTER:								
	Quantity : 1No.								
	Capacity : 1000 LPH								
	MOC & Make of Housing : UKL								
	MOC & Make of Cartridge : UKL								
	Capcity : 100 LPH								
	MOC & Make of Vessel : UKL								
	Diameter : 40 mm								
	Type of Valve : Single Multiport								
	media : Support bed + Sand								
	MICRON CARTRIDGE FILTER :								
	Quantity : 1 Set.								
	Filter Rating : 5 Microns								
	Size : 20 " Long								
	ANTISCALANT DOSING PUMPS:								
	Quanity : 1 Set								
	Type : Electro - magnetic								
	Capacity : 1.5 LPH @ 4 Bar								
	HIGH PRESSURE PUMP:								
	Quantity : 1 No								
	Capacity : 1700 LPH								
	Type of Pump : Vertical Multistage Centrigugal Pump								
	MOC : SS 304								
	Motor Rating : 2 HP, 3 Phase								
	Maximum Pressure : 12 Kg/ cm2								
	Make : UKL								
	RESERVE OSMOSIS SYSTEM :								
	Quantity : 1 No								
	Capacity : 1000 LPH								
	Module Type								
	Membrane Specifications {Polyamde}								
	Make of Membrane : UKL								
	UV STERILISER								
	Max. Treatment Flow : 1 m3/hr								
	No. of Lamps : 1 No								
	Wattage : 39 W								
	Efficiency : 99.99%								
	Material of Construction : SS 304								
	PRODUCT WATER QUALITY:								
	Appearance : Crystal Clear								

Scanned by CamScanner

Scanned by CamScanner

ವಿಷಯ :

ಪಂಕ್ತಿಯ ಸಂಖ್ಯೆ	

Sl No								
	Abide by the ISO Standards							
	S S Tank : 304 Grade with 16 guage 2000 liters Capacity							
	304 Grade 10 Gauage SS Pipe (with stream valve) 25 Ft							
	COIN BOOTH DISPENSING UNIT							
	for 5 Liters & 20 Ltrs Separately							
	Raw Water Stoage Tank : Dunction - for Storage of Raw Water							
	Type / MOC : Two / Three Layered PE tanks White / Transparent in color made from virgin material of food grade							
	Quality suitabke fir the purpose of providing							
	Storage Drinking / Portable Water : 5000 Liters Capacity							
55	KSRB 7.5 : Providing and fixing **pull and push type rolling shutters** of approved make out of 18 guage, 75mm wide cold rolled steel laths of convex corrugation, with side guides and bottom rail, with interlocking arrangements for steel laths by means of alternate clips, suspension shaft with High tension coil type springs two numbers, mounted on specially designed pipe shaft, with bracket plates, guide channels, ball bearing arrangements, for inside & outside locking with push & pull operations complete including pulling hooks, 4Nos. handles with all fittings and accessories, painted with a coat of red lead paint (without top cover) cost of materials, labour, HOM of machinery complete as per specifications. **Shutter size 3mx2.8 m**. etc., complete and as per the directions of the Engineer-in-charge of the work.							
	BESCOM Charges							
								Total

Certificate:

1. The above work done satisfactory and no materials issued from departmentally.

25/10/2017

Original/Duplicate/Triplicate

...CT CERTIFICATE.

...2017

Previous Measurement		Present Measurement			Total Upto Date		
Qty.	Cost	Qty.	Rate Rs. P.	Amount	Qty	Cost	Remarks
-	-						
-	-						
-	-						
-	-						
-	-						
-	-						
-	-						
-	-	1.00	920000.00	920000.00	1.00	920000.00	
-	-	6.48	2892.83	18746.00	6.48	18746.00	
				10000.00		10000.00	
				1409814.00		1409814.00	

Limited to as per Modified work Order Amount → 1400167=00

1408982=00

1408982=00

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
